

2018 Annual Reviews

County Council Hearing – November 6, 2018

Complete Streets

Public Services Center, 6th Floor Hearing Rm., 1300 Franklin St., Vancouver, WA

Gary Albrecht, Community Planning





2003 - 2008 Transportation Improvement Program

Project: K. NE Padden Parkway - Andresen Road to NE 94th Avenue

Vicinity Map




Project Summary

Work Order Number:	392722	Federal Aid Number:	NA
Project Manager:	Matt Hall		
Project Description:	Improve to 4-lane principal arterial parkway with a separated bicycle / pedestrian trail.		
Project Length (mi.):	1.07		
Basis for Project:	Completion of Padden Parkway Corridor		
Timeline:	PE - Pre 2003; ROW - Pre 2003; CN - Pre 2003 - 2003		
Notes:			
Status (November):	Road portion improvements are open to traffic. Construction continues on the pedestrian bridge with completion expected late next summer.		


Cross-Section Detail

4-lane Principal Arterial Parkway
with regional trail

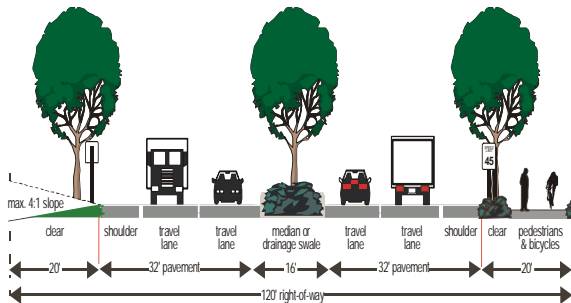

Project Cost Summary


Engineering	\$795,000
Real Property	\$50,000
Construction	\$6,200,000
Total:	\$7,045,000



■ Engineering
■ Real Property
■ Construction

Funding Summary

County Road Fund:	\$1,545,000
TIF:	\$300,000
Federal Grant:	\$2,300,000
State Grant:	\$0
Loan:	\$2,900,000
Other:	\$0
Projected Grants:	\$0
Beyond Six-Year:	\$0
Total:	\$7,045,000



■ CRF
■ TIF
■ All Other





2013 - 2018 Transportation Improvement Program

Project: D. NE 119th Street - NE 72nd Avenue to NE 87th Avenue

Vicinity Map




Project Summary

Project Number:	390722	Project Length (mi.):	1.23
Project Manager:	Robin Washington	Client:	Susan Wilson
Basis for Project:	Economic Development, Urban Holding corridor.		
Timeline:	PE Pre 2013-2014; ROW Pre 2013-2014; CN 2014-2015		
Project Description:	Improve to 4-lane minor arterial with center turn lane/median, bike lanes, and sidewalks.		

Notes:


Status: Design and right-of-way land acquisition in progress.

Cross-Section Detail

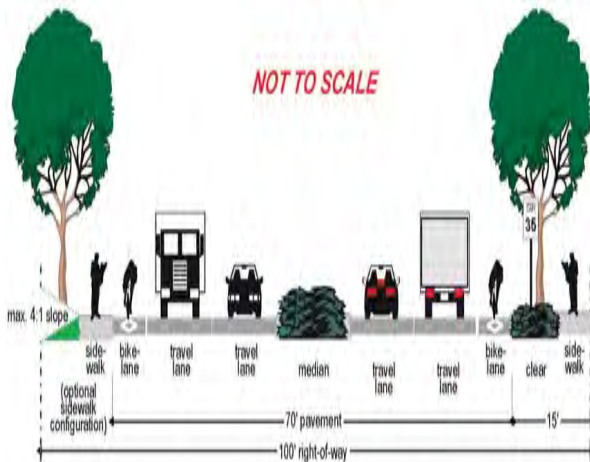

Project Cost Summary

Engineering:	\$1,143,000
Real Property:	\$4,204,000
Construction:	\$16,500,000
Total:	\$21,847,000



Engineering
Real Property
Construction

Funding Summary

County Road Fund:	\$12,774,000
TIF:	\$3,761,000
Federal Grant:	\$2,446,000
State Grants:	\$0
Loan:	\$0
Other:	\$1,366,000
Projected Funds:	\$1,500,000
Unfunded:	\$0
Total:	\$21,847,000



CRF
TIF
All Other Funds





2013 - 2018 Transportation Improvement Program

Project: B. NE 10th Avenue - NE 141st Street to NE 149th Street

Vicinity Map




Project Summary

Project Number:	312522	Project Length (mi.):	0.73
Project Manager:	Jean Singer	Client:	Susan Wilson
Basis for Project:	Safety, Safety and traffic circulation		
Timeline:	PE Pre 2013-2013; ROW Pre 2013; CN 2013-2014		
Project Description:	Improve to 2-lane collector with center turn lane, bike lanes, and sidewalks.		

Notes:

Status: Design complete and real-estate acquisition 99% complete. Construction will begin in spring 2013.

Cross-Section Detail

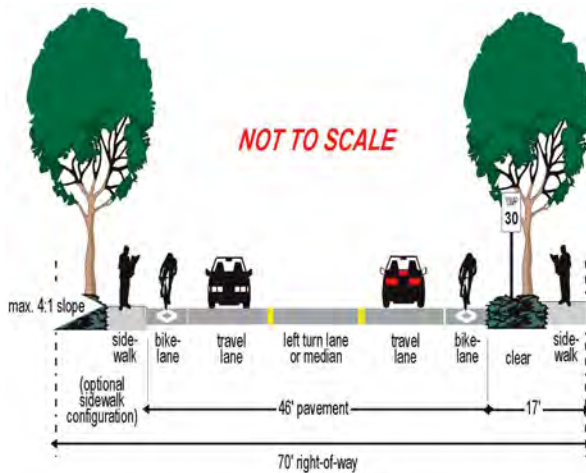


Project Cost Summary


Engineering:	\$282,000
Real Property:	\$895,000
Construction:	\$3,745,000
Total:	\$4,922,000

Funding Summary

County Road Fund:	\$403,000
TIF:	\$140,000
Federal Grant:	\$2,640,000
State Grants:	\$1,697,000
Loan:	\$0
Other:	\$0
Projected Funds:	\$42,000
Unfunded:	\$0
Total:	\$4,922,000



Engineering
Real Property
Construction



CRF
TIF
All Other Funds





2003 - 2008 Transportation Improvement Program

Project: F. NE 25th Avenue - NE 78th Street to NE 99th Street

Vicinity Map




Project Summary

Work Order Number:	382722	Federal Aid Number:	NA
Project Manager:	Carolyn Heniges		
Project Description:	Improve to 2-lane collector with center turn lane, bike lanes, and sidewalks; Install signal at NE 88th Street.		
Project Length (mi.):	0.93		
Basis for Project:	Accommodate traffic growth; Improve bicycle and pedestrian access; Improve walkway access to Gaiser Middle School		
Timeline:	PE - Pre 2003; ROW - Pre 2003; CN - Pre 2003 - 2003		
Notes:			
Status (November):	Construction is nearly complete.		

Cross-Section Detail


2-lane Collector

with center/left turn lane and bike lanes

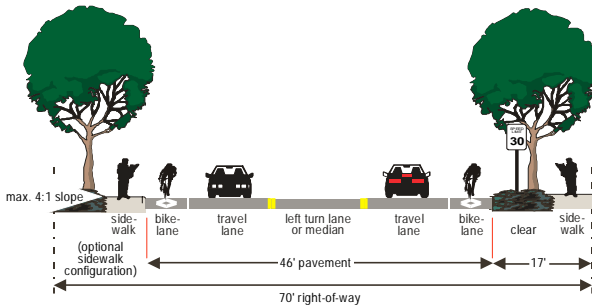

Project Cost Summary

Engineering	\$696,000
Real Property	\$2,446,000
Construction	\$4,160,000
Total:	\$7,302,000



Funding Summary

County Road Fund:	\$5,452,738
TIF:	\$1,849,262
Federal Grant:	\$0
State Grant:	\$0
Loan:	\$0
Other:	\$0
Projected Grants:	\$0
Beyond Six-Year:	\$0
Total:	\$7,302,000

